


ADD BIRD SCREEN TO OPEN END 90.

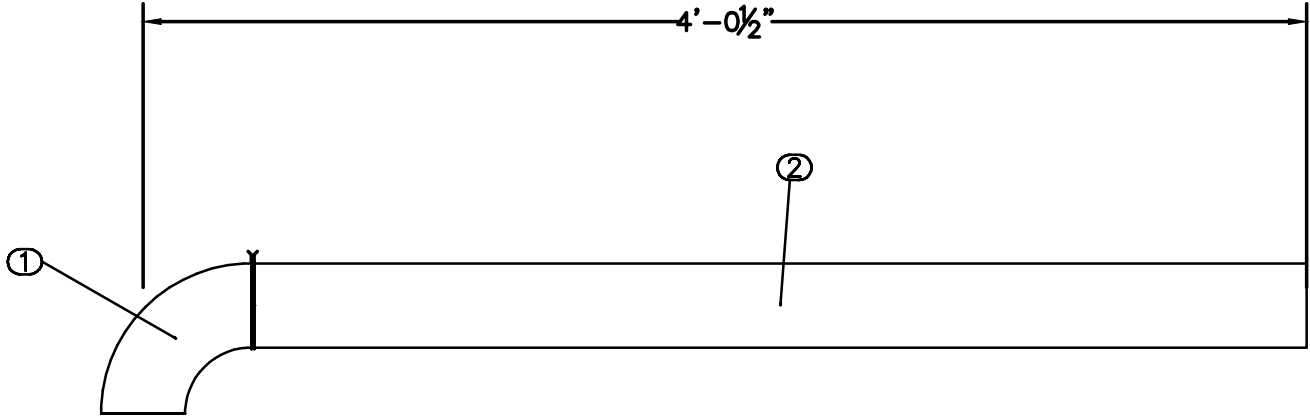

Murphy—PFFS—SPOOL—BOM							
Mark	Qty	Description	End 1	End 2	Lft	LDec	Size
1	1	Std Wt SA234 WPB CS BW LR 90 Deg El					3
2	1	Sch 40 SA-53B CS Smls Pipe PE	BEV	BEV	3'-7 7/8"	43.852	3

MURPHY

CONSTRUCTORS

ENGINEERS

MECHANICAL

INDUSTRIAL

1233 N. Price Rd.

St. Louis, MO 63132-2303

314-997-6600 phone

BIMCAD@murphy-stl.com

DRN JMM

5/18/2021

CHK

APP

JOB NO.

210140

REF.DWG.

DRAWING NO./TRACKING NO.

210140-A-UPL2-117

WUSM RESEARCH BUILDING

NRB CUP

LVLO2 SPOOLS

SERVICE NAME

HRC VENT

QTY.

1

SHT/NO

1 of 1

REV

0

QA/QC ACCEPT

FLANGE WEIGHT/ORIENTATION

☐

FITTING ORIENTATION

☐

BOLTS/CPLG'S/TH'D TIGHT

☐

SPOOL IDENTIFICATION

☐

SPEC.

NA

ASME

NA

X-RAY

NA

HYDRO TEST

NA

PWHT

NA

COMMENTS

MURPHY WPS#

REV

0

DATE

DESCRIPTION

DRN

CHK

APP
